


Exhibit VIII. C.20.a


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Calendar																		
							ter	3rd Quarter			1st Quarter			3rd Quarter			1st Quarter			3rd Quarter			1st Quarter		
							Apr	Jul	Oct	Jan	Apr	Jul	Oct	Jan	Apr	Jul	Oct	Jan	Apr	Jul	Oct	Jan	Apr	Jul	
1		Preconstruction	138 days	Tue 7/1/14	Thu 1/8/15																				
2	✓	Notice to Proceed to Master Planner	0 days	Tue 7/1/14	Tue 7/1/14																				
3		Secure Financing	24 wks	Tue 7/1/14	Mon 12/15/14																				
4		Set Baseline Budget and Schedule	1 wk	Tue 7/1/14	Mon 7/7/14																				
5		Finalize Responsibility Matrix	2 wks	Tue 7/1/14	Mon 7/14/14																				
6		Issue RFP for Architect and Engineer	20 days	Tue 7/1/14	Mon 7/28/14																				
7		RFP Review and Award	5 days	Tue 7/29/14	Mon 8/4/14	6																			
8		Schematics and Background by Master Planner	25 days	Tue 7/1/14	Mon 8/4/14																				
9		Architectural Drawings Civil / Structural / Utilities	60 days	Tue 8/5/14	Mon 10/27/14	7																			
10		Architectural Drawings Architectural	80 days	Tue 8/5/14	Mon 11/24/14	7																			
11		Architectural Drawings MEPs	80 days	Tue 8/5/14	Mon 11/24/14	7																			
12		Owner Design Review	10 days	Tue 11/25/14	Mon 12/8/14	10																			
13		Finalize Design	10 days	Tue 12/9/14	Mon 12/22/14	12																			
14		File for Permits Civil / Structural / Utilities	25 days	Tue 10/28/14	Mon 12/1/14	9																			
15		File for Permits Architectural	25 days	Tue 11/25/14	Mon 12/29/14	10																			
16		File for Permits MEP	25 days	Tue 11/25/14	Mon 12/29/14	11																			
17		License is Issued	0 days	Thu 1/1/15	Thu 1/1/15																				
18		Full Property Secured	5 days	Fri 1/2/15	Thu 1/8/15																				
19		Bidding and Buyout	47.5 days	Tue 12/30/14	Thu 3/5/15																				
20		Create Bid Packages	2 wks	Tue 12/30/14	Mon 1/12/15	15																			
21		Send out for Bids	3 wks	Tue 1/13/15	Mon 2/2/15	20																			
22		Receive and Level Bids	2 wks	Tue 2/3/15	Mon 2/16/15	21																			
23		Negotiate with Selected Contractors	1 wk	Tue 2/17/15	Mon 2/23/15	22																			
24		Finalize Awards and Contracts	1.5 wks	Tue 2/24/15	Thu 3/5/15	23																			
25		General Conditions	17 days	Fri 3/6/15	Mon 3/30/15																				
26		Subcontractors Notice to Proceed	1 day	Fri 3/6/15	Fri 3/6/15																				
27		Submit insurance documents	1 wk	Mon 3/9/15	Fri 3/13/15	26																			
28		Prepare and submit final project schedule	2 wks	Mon 3/9/15	Fri 3/20/15	26																			
29		Prepare and submit schedule of values	1 wk	Mon 3/9/15	Fri 3/13/15	26																			
30		Submit preliminary shop drawings	2 wks	Mon 3/9/15	Fri 3/20/15	26																			
31		Submit monthly requests for payment	1 day	Mon 3/30/15	Mon 3/30/15	26FS+15 days																			
32		Final Budget and Schedule of Values GC	1 wk	Mon 3/16/15	Fri 3/20/15	29																			
33		Long Lead Procurement	80 days	Thu 1/1/15	Wed 4/22/15																				
34		Order pumps and water reclamation equipment	16 wks	Thu 1/1/15	Wed 4/22/15	17																			
35		Order steel	16 wks	Thu 1/1/15	Wed 4/22/15	17																			
36		Order elevator equipment	16 wks	Thu 1/1/15	Wed 4/22/15	17																			
37		Order HVAC units	16 wks	Thu 1/1/15	Wed 4/22/15	17																			

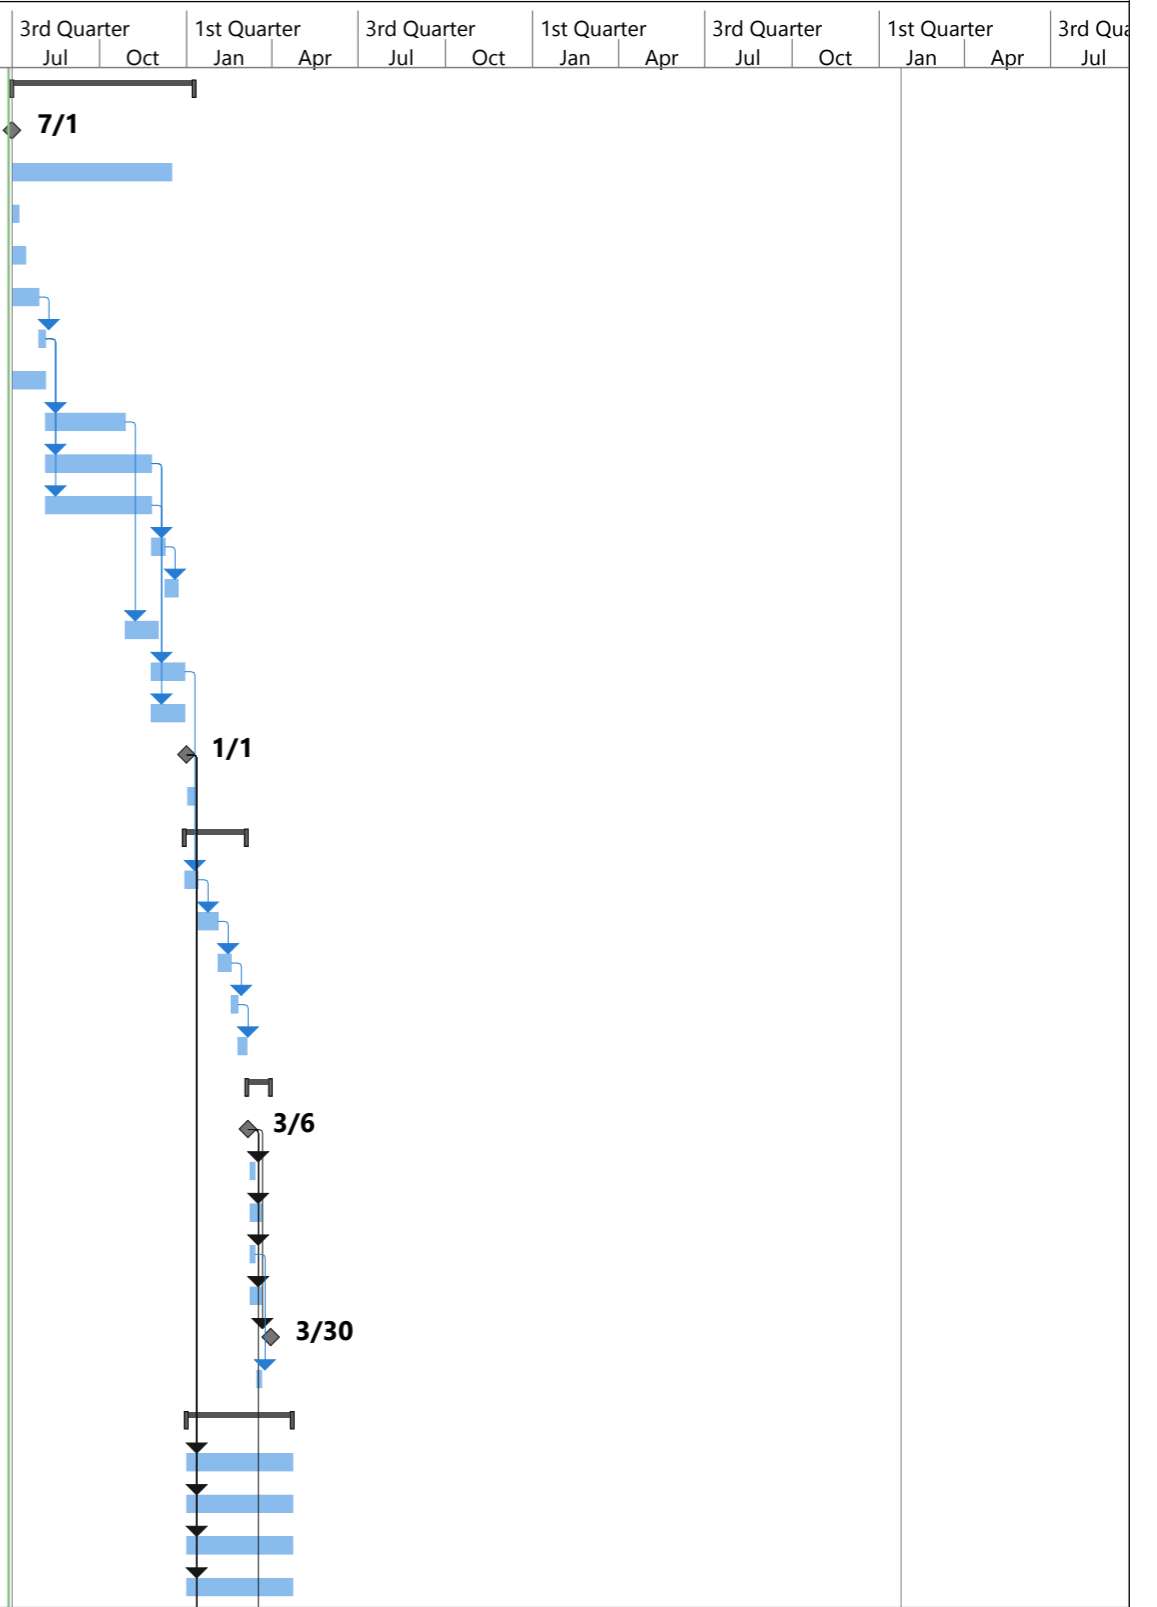

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

Exhibit VIII. C.20.a

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	3rd Quarter			1st Quarter		3rd Quarter			1st Quarter		3rd Quarter			1st Quarter		3rd Quarter		
							Apr	Jul	Oct	Jan	Apr	Jul	Oct	Jan	Apr	Jul	Oct	Jan	Apr	Jul	Oct	Jan	Apr	Jul
38		Order generators	16 wks	Thu 1/1/15	Wed 4/22/15	17																		
39		Order UPS equipment	16 wks	Thu 1/1/15	Wed 4/22/15	17																		
40		Order substation equipment	16 wks	Thu 1/1/15	Wed 4/22/15	17																		
41		Mobilize on Site	15 days	Mon 1/5/15	Fri 1/23/15																			
42		Groundbreaking	0 days	Mon 1/5/15	Mon 1/5/15																			
43		Install temporary power service	1 wk	Mon 1/5/15	Fri 1/9/15	42																		
44		Install temporary water service	1 wk	Mon 1/5/15	Fri 1/9/15	42																		
45		Install temporary sewer line	2 wks	Mon 1/5/15	Fri 1/16/15	42																		
46		Set up site office	1 wk	Mon 1/19/15	Fri 1/23/15	43,45																		
47		Set line and grade benchmarks	1 wk	Mon 1/5/15	Fri 1/9/15	42																		
48		Prepare site - lay down yard and temporary fencing	2 wks	Mon 1/5/15	Fri 1/16/15	42																		
49		Roadwork	250 days	Mon 1/5/15	Fri 12/18/15																			
50		Interchange 15b	50 wks	Mon 1/5/15	Fri 12/18/15	42																		
51		Roundabout 17/17A	36 wks	Mon 1/5/15	Fri 9/11/15	42																		
52		Utility line route 17A	12 wks	Mon 1/5/15	Fri 3/27/15	42																		
53		Roundabout Casino entrance	10 wks	Mon 1/5/15	Fri 3/13/15	42																		
54		Causeway	16 wks	Mon 1/5/15	Fri 4/24/15	42																		
55		Existing site entrance	4 wks	Mon 4/27/15	Fri 5/22/15	54																		
56		Service road widening and work	16 wks	Mon 1/5/15	Fri 4/24/15	42																		
57		Electrical Substation and Feeds	150 days	Mon 1/5/15	Fri 7/31/15																			
58		Excavate for foundations and underground	2 wks	Mon 1/5/15	Fri 1/16/15	42																		
59		Sleeve for HV feed	1 day	Mon 1/19/15	Mon 1/19/15	58																		
60		Pour Foundations and slab	2 wks	Tue 1/20/15	Mon 2/2/15	59																		
61		Set substation equipment	8 wks	Tue 2/3/15	Mon 3/30/15	60																		
62		Bring in HV line	1 wk	Tue 3/31/15	Mon 4/6/15	61																		
63		Set new duct banks	16 wks	Mon 1/19/15	Fri 5/8/15	58																		
64		Pull feeds thru duct banks to new central plants	12 wks	Mon 5/11/15	Fri 7/31/15	63																		
65		Inspections	12 wks	Mon 5/11/15	Fri 7/31/15	63																		
66		Site Grading and Utilities	120 days	Mon 1/5/15	Fri 6/19/15																			
67		Clear and grub site	4 wks	Mon 1/5/15	Fri 1/30/15	42																		
68		Stone site access and temporary parking area	2 wks	Mon 1/5/15	Fri 1/16/15	42																		
69		Excavate for foundations	4 wks	Mon 1/5/15	Fri 1/30/15	42																		
70		Blasting and rock removal	8 wks	Mon 2/2/15	Fri 3/27/15	69																		
71		Install storm drainage	12 wks	Mon 2/2/15	Fri 4/24/15	69																		
72		Set site silt protection	2 wks	Mon 4/27/15	Fri 5/8/15	71																		
73		Excavate electrical duct banks	12 wks	Mon 1/5/15	Fri 3/27/15	42																		
74		Excavate for water reclamation lines	8 wks	Mon 1/5/15	Fri 2/27/15	42																		

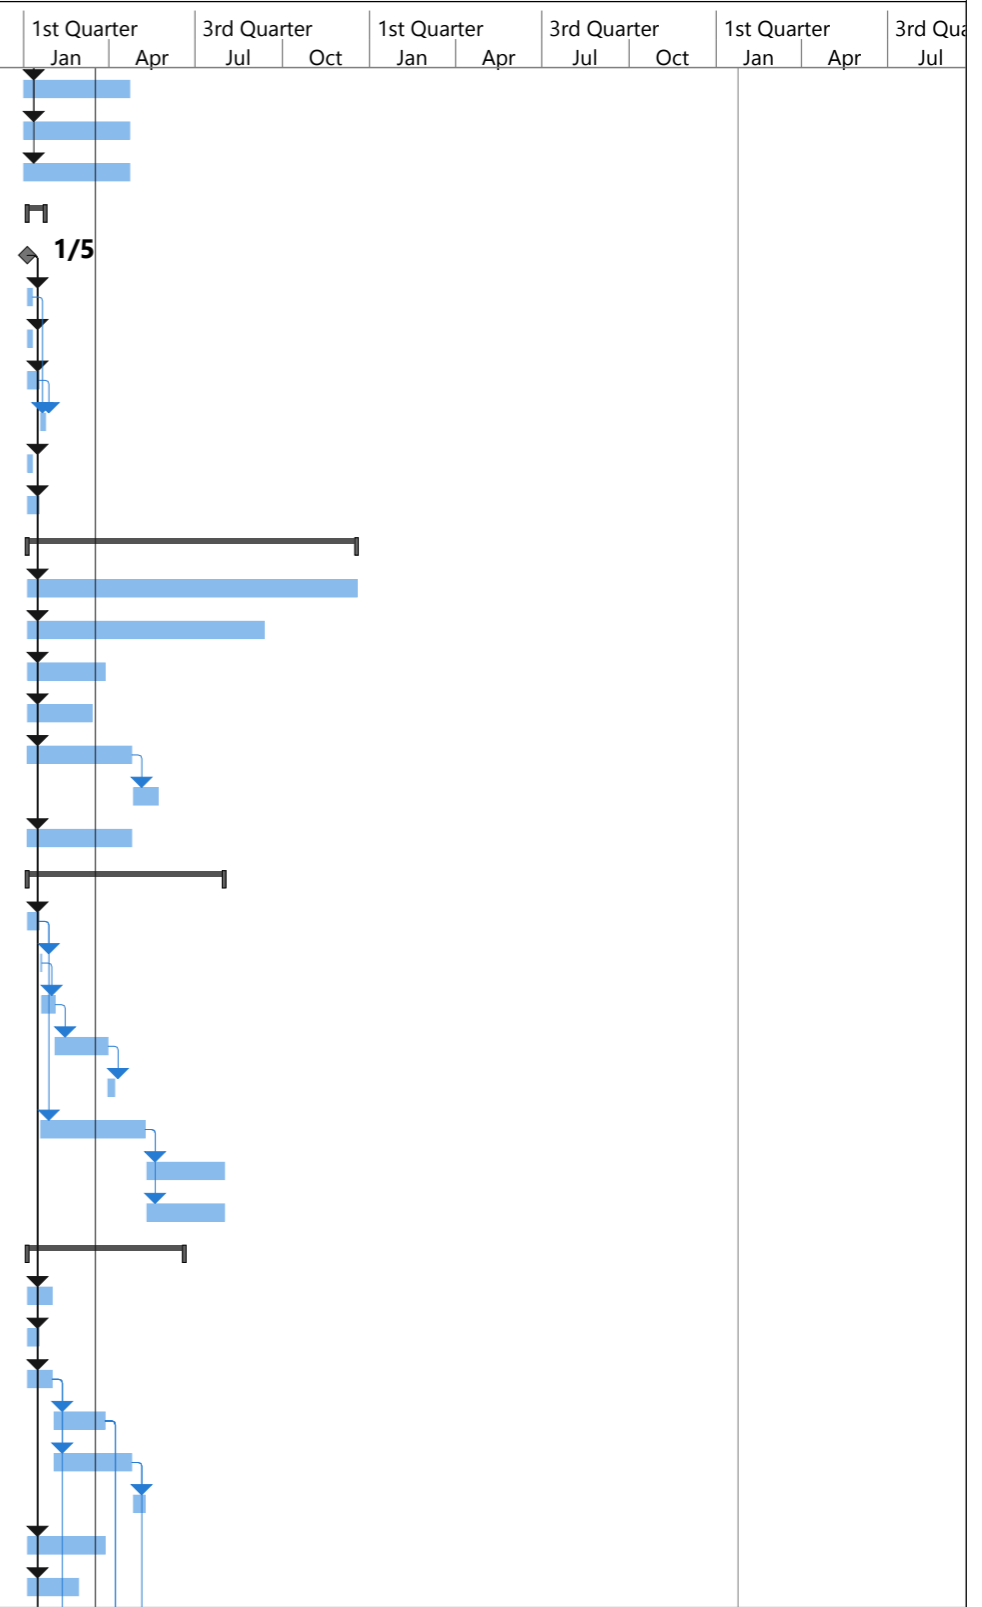

Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

Exhibit VIII. C.20.a

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Timeline															
							ter Apr	3rd Quarter Jul Oct	1st Quarter Jan Apr	3rd Quarter Jul Oct	1st Quarter Jan Apr	3rd Quarter Jul Oct	1st Quarter Jan Apr	3rd Quarter Jul Oct								
75		Excavate for fire line	4 wks	Mon 2/2/15	Fri 2/27/15	69																
76		Set benchmarks and layout building	2 wks	Mon 1/5/15	Fri 1/16/15	42																
77		Backfill and final grade	8 wks	Mon 4/27/15	Fri 6/19/15	71																
78		Water reclamation facility	205 days	Mon 1/5/15	Fri 10/16/15																	
79		Excavate foundations	1 wk	Mon 1/5/15	Fri 1/9/15	42																
80		Begin underground work	4 wks	Mon 1/12/15	Fri 2/6/15	79																
81		Trench to old sewage treatment facility	4 wks	Mon 1/5/15	Fri 1/30/15	42																
82		Concrete	2 wks	Mon 1/12/15	Fri 2/20/15	80																
83		CMU Walls	4 wks	Mon 2/23/15	Fri 3/20/15	82																
84		Set Roof	2 wks	Mon 3/23/15	Fri 4/3/15	83																
85		Mechanical rough	12 wks	Mon 4/6/15	Fri 6/26/15	84																
86		Electrical Rough	12 wks	Mon 4/6/15	Fri 6/26/15	84																
87		Plumbing Rough	20 wks	Mon 4/6/15	Fri 8/21/15	84																
88		Set half of new equipment	8 wks	Mon 8/24/15	Fri 10/16/15	87																
89		Powerup set equipment	1 wk	Mon 6/29/15	Fri 7/3/15	86																
90		Demolish old facility	4 wks	Mon 7/6/15	Fri 7/31/15	89																
91		Set remaining equipment	8 wks	Mon 7/6/15	Fri 8/28/15	89																
92		Casino and Hotel	476 days	Mon 3/30/15	Mon 1/23/17																	
93		Foundations	60 days	Mon 3/30/15	Fri 6/19/15																	
94		Area 1 footings and piers	6 wks	Mon 3/30/15	Fri 5/8/15	70																
95		Area 1 slab	2 wks	Mon 5/11/15	Fri 5/22/15	94																
96		Area 2 footings and piers	8 wks	Mon 3/30/15	Fri 5/22/15	70																
97		Area 2 slab	2 wks	Mon 5/25/15	Fri 6/5/15	96																
98		Area 3 footings and piers	10 wks	Mon 3/30/15	Fri 6/5/15	70																
99		Area 3 slab	2 wks	Mon 6/8/15	Fri 6/19/15	98																
100		Area 4 footings and piers	6 wks	Mon 3/30/15	Fri 5/8/15	70																
101		Area 4 slab	2 wks	Mon 5/11/15	Fri 5/22/15	100																
102		Area 5 footings and piers	6 wks	Mon 3/30/15	Fri 5/8/15	70																
103		Area 5 slab	2 wks	Mon 5/11/15	Fri 5/22/15	102																
104		Area 6 footings and piers	6 wks	Mon 3/30/15	Fri 5/8/15	70																
105		Area 6 slab	2 wks	Mon 5/11/15	Fri 5/22/15	104																
106		Underground electrical and plumbing	8 wks	Mon 3/30/15	Fri 5/22/15	70																
107		Core and Shell	245 days	Mon 5/11/15	Fri 4/15/16																	
108		Area 1 steal	12 wks	Mon 5/25/15	Fri 8/14/15	95																
109		Area 1 hollow core plank	8 wks	Mon 6/22/15	Fri 8/14/15	108FS-8 wks																
110		Area 1 set modular hotel rooms	4 wks	Mon 7/27/15	Fri 8/21/15	108FS-3 wks																
111		Area 1 pour inner corridor	4 wks	Mon 8/3/15	Fri 8/28/15	108FS-2 wks																



Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

Exhibit VIII. C.20.a

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	3rd Quarter			1st Quarter		3rd Quarter			1st Quarter		3rd Quarter		1st Quarter		3rd Quarter	
							Apr	Jul	Oct	Jan	Apr	Jul	Oct	Jan	Apr	Jul	Oct	Jan	Apr	Jul		
149		Interior Framing and Doors	140 days	Mon 10/19/15	Fri 4/29/16																	
150		Install interior stud walls and drywall	20 wks	Mon 10/19/15	Fri 3/4/16	138FS-10 wks																
151		Frame and install soffits and drywall	20 wks	Mon 11/2/15	Fri 3/18/16	138FS-8 wks																
152		Install interior doors and hardware	6 wks	Mon 3/21/16	Fri 4/29/16	151																
153		Install interior specialty doors	6 wks	Mon 3/7/16	Fri 4/15/16	150																
154		Hotel Finishes	230 days	Mon 1/25/16	Fri 12/9/16																	
155		Install millwork and wood trim	12 wks	Mon 4/4/16	Fri 6/24/16	152FS-4 wks																
156		Paint walls and woodwork	16 wks	Mon 4/4/16	Fri 7/22/16	152FS-4 wks																
157		Install ceiling grid	20 wks	Mon 1/25/16	Fri 6/10/16	151FS-8 wks																
158		Install ceiling tile	20 wks	Mon 4/4/16	Fri 8/19/16	157FS-10 wks																
159		Hang wallpaper	20 wks	Mon 5/2/16	Fri 9/16/16	156FS-12 wks																
160		Install building carpet	20 wks	Mon 5/16/16	Fri 9/30/16	156FS-10 wks																
161		Install accessories	20 wks	Mon 7/25/16	Fri 12/9/16	159FS-8 wks																
162		Themeing elements	10 wks	Mon 10/3/16	Fri 12/9/16	160																
163		Casino Floor	220 days	Mon 12/28/15	Fri 10/28/16																	
164		Frame columns and soffits	18 wks	Mon 12/28/15	Fri 4/29/16	138																
165		Hang ceilings	14 wks	Mon 2/22/16	Fri 5/27/16	164FS-10 wks																
166		Paint and finishes	18 wks	Mon 3/7/16	Fri 7/8/16	164FS-8 wks																
167		Pull lighting power	14 wks	Mon 12/28/15	Fri 4/1/16	138																
168		Pull ceiling LV	14 wks	Mon 12/28/15	Fri 4/1/16	138																
169		Install access floor	12 wks	Mon 12/28/15	Fri 3/18/16	138																
170		Carpet	10 wks	Mon 2/8/16	Fri 4/15/16	169FS-6 wks																
171		Layout of machine locations	8 wks	Mon 3/21/16	Fri 5/13/16	170FS-4 wks																
172		Coredrill floor	10 wks	Mon 4/18/16	Fri 6/24/16	171FS-4 wks																
173		Pull game power	10 wks	Mon 5/16/16	Fri 7/22/16	172FS-6 wks																
174		Pull floor LV	10 wks	Mon 5/16/16	Fri 7/22/16	172FS-6 wks																
175		Set bases	10 wks	Mon 6/13/16	Fri 8/19/16	174FS-6 wks																
176		Install machines	10 wks	Mon 7/11/16	Fri 9/16/16	175FS-6 wks																
177		Set chairs	10 wks	Mon 8/8/16	Fri 10/14/16	176FS-6 wks																
178		Testing	2 wks	Mon 10/17/16	Fri 10/28/16	177																
179		Restaurant, Spa, Meeting Rooms and Amenities	80 days	Mon 6/27/16	Fri 10/14/16																	
180		Finishes	16 wks	Mon 6/27/16	Fri 10/14/16	158FS-8 wks																
181		Back of House	50 days	Mon 6/27/16	Fri 9/2/16																	
182		Finishes	10 wks	Mon 6/27/16	Fri 9/2/16	158FS-8 wks																
183		FF&E	95 days	Mon 8/15/16	Fri 12/23/16																	
184		Hotel rooms	16 wks	Mon 9/5/16	Fri 12/23/16																	
185		Offices	4 wks	Mon 10/3/16	Fri 10/28/16																	



Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

Exhibit VIII. C.20.a


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	3rd Quarter			1st Quarter		3rd Quarter			1st Quarter		3rd Quarter		1st Quarter		3rd Qu
							Apr	Jul	Oct	Jan	Apr	Jul	Oct	Jan	Apr	Jul	Oct	Jan	Apr	Jul	
186		Workstations	8 wks	Mon 9/5/16	Fri 10/28/16																
187		Restourants	16 wks	Mon 8/15/16	Fri 12/2/16																
188		Spa	8 wks	Mon 10/10/16	Fri 12/2/16																
189		Pools / Gardens	4 wks	Mon 11/7/16	Fri 12/2/16																
190		Fitness Center	4 wks	Mon 11/7/16	Fri 12/2/16																
191		Lounges	2 wks	Mon 11/21/16	Fri 12/2/16																
192		Meeting Rooms	4 wks	Mon 11/7/16	Fri 12/2/16																
193		Elevators	260 days	Mon 6/22/15	Fri 6/17/16																
194		Set elevator equipment in shafts	30 wks	Mon 6/22/15	Fri 1/15/16	143FS-12 wks															
195		Set equipment in mechanical room	20 wks	Mon 1/18/16	Fri 6/3/16	194															
196		Test and align doors and equipment	2 wks	Mon 6/6/16	Fri 6/17/16	195															
197		Central Plant	100 days	Mon 12/28/15	Fri 5/13/16																
198		Set electrical equipment	12 wks	Mon 12/28/15	Fri 3/18/16	138															
199		Set hvac equipment	12 wks	Mon 2/22/16	Fri 5/13/16	198FS-4 wks															
200		Rough in electrical	8 wks	Mon 12/28/15	Fri 2/19/16	138															
201		Rough in plumbing	8 wks	Mon 12/28/15	Fri 2/19/16	138															
202		Rough in hvac	6 wks	Mon 12/28/15	Fri 2/5/16	138															
203		Rough in sprinkler	6 wks	Mon 12/28/15	Fri 2/5/16	138															
204		Set fire pump	2 wks	Mon 2/8/16	Fri 2/19/16	203															
205		Plumbing	250 days	Mon 12/28/15	Fri 12/9/16																
206		Rough-in plumbing	34 wks	Mon 12/28/15	Fri 8/19/16	138															
207		Tie-in fire line riser and set valves	12 wks	Mon 8/22/16	Fri 11/11/16	206															
208		Set plumbing fixtures and trim	24 wks	Mon 5/30/16	Fri 11/11/16	206FS-12 wks															
209		Flush, test, and clean piping and fixtures	4 wks	Mon 11/14/16	Fri 12/9/16	208															
210		Gas rough in	36 wks	Mon 12/28/15	Fri 9/2/16	138															
211		Gas tie ins	12 wks	Mon 9/5/16	Fri 11/25/16	210															
212		Electrical	250 days	Mon 12/28/15	Fri 12/9/16																
213		BOH electrical rough	36 wks	Mon 12/28/15	Fri 9/2/16	138															
214		Hotel room electrical	36 wks	Mon 12/28/15	Fri 9/2/16	138															
215		Restourant electrical	36 wks	Mon 12/28/15	Fri 9/2/16	138															
216		BOH LV	36 wks	Mon 12/28/15	Fri 9/2/16	138															
217		Hotel LV	36 wks	Mon 12/28/15	Fri 9/2/16	138															
218		Restourant LV	36 wks	Mon 12/28/15	Fri 9/2/16	138															
219		Electrical finishes	24 wks	Mon 6/27/16	Fri 12/9/16	213FS-10 wks															
220		Heating and Ventilating - AC	250 days	Mon 12/28/15	Fri 12/9/16																
221		Rough-in mechanical	36 wks	Mon 12/28/15	Fri 9/2/16	138															
222		Set airhandlers in mezzanine	24 wks	Mon 4/18/16	Fri 9/30/16	221FS-20 wks															



Task		Project Summary		Manual Task		Start-only		Deadline	
Split		Inactive Task		Duration-only		Finish-only		Progress	
Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
Summary		Inactive Summary		Manual Summary		External Milestone			

Exhibit VIII. C.20.a

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Calendar																	
							ter	3rd Quarter			1st Quarter			3rd Quarter			1st Quarter			3rd Quarter			1st Quarter	
							Apr	Jul	Oct	Jan	Apr	Jul	Oct	Jan	Apr	Jul	Oct	Jan	Apr	Jul	Oct	Jan	Apr	Jul
223		Set hotel room units	36 wks	Mon 12/28/15	Fri 9/2/16	138																		
224		Set kitchen hoods and exhaust	20 wks	Mon 3/7/16	Fri 7/22/16	150																		
225		Set HVAC trim and test and balance system	22 wks	Mon 7/11/16	Fri 12/9/16	221FS-8 wks																		
226		Final Clean-up and Occupancy	10 days	Fri 12/9/16	Fri 12/23/16																			
227		Remove debris from building and do final clean-up	2 wks	Mon 12/12/16	Fri 12/23/16	225																		
228		Substantial completion date	0 days	Fri 12/9/16	Fri 12/9/16	225																		
229		Temporary Approval of Occupancy	0 days	Fri 12/9/16	Fri 12/9/16	228																		
230		Complete Final Inspections	135 days	Mon 6/20/16	Fri 12/23/16																			
231		Complete elevator inspection and certification	4 wks	Mon 6/20/16	Fri 7/15/16	196																		
232		Perform architect's inspection	2 wks	Mon 12/12/16	Fri 12/23/16	225																		
233		Perform local building agency inspection	2 wks	Mon 12/12/16	Fri 12/23/16	225																		
234		Perform Fire Marshal's inspection	2 wks	Mon 12/12/16	Fri 12/23/16	225																		
235		Operations	15 days	Mon 12/12/16	Fri 12/30/16																			
236		Training	2 wks	Mon 12/12/16	Fri 12/23/16	229																		
237		Soft Opening	1 wk	Mon 12/26/16	Fri 12/30/16	236																		
238		Grand Opening	0 days	Fri 12/30/16	Fri 12/30/16	237																		
239		Closeout	31 days	Mon 12/12/16	Mon 1/23/17																			
240		Complete punch list items from all inspections	2 wks	Mon 12/12/16	Fri 12/23/16	225																		
241		Obtain certificate of occupancy	0 days	Fri 12/23/16	Fri 12/23/16	240																		
242		Issue final completion documents including warrant	4 wks	Mon 12/26/16	Fri 1/20/17	241																		
243		Issue final request for payment	1 day	Mon 1/23/17	Mon 1/23/17	242																		
244		Permanent Operations Financing Secured	0 days	Mon 1/23/17	Mon 1/23/17	243																		
245		Site Finishes	100 days	Mon 4/4/16	Fri 8/19/16																			
246		Planting sprinklers	16 wks	Mon 4/4/16	Fri 7/22/16																			
247		Site plantings	12 wks	Mon 5/30/16	Fri 8/19/16	246FS-8 wks																		
248		Pavers and walkways	12 wks	Mon 4/4/16	Fri 6/24/16																			
249		Sod and seed	8 wks	Mon 6/27/16	Fri 8/19/16	248																		
250		Pave, curb, and stripe parking lot	20 wks	Mon 4/4/16	Fri 8/19/16																			
251		GrassPave west lot	16 wks	Mon 4/4/16	Fri 7/22/16																			
252		GrassPave central lot	16 wks	Mon 4/4/16	Fri 7/22/16																			
253		Garage	190 days	Mon 12/28/15	Fri 9/16/16	138																		
254		Final Excavation	4 wks	Mon 12/28/15	Fri 1/22/16	138																		
255		Pour Concrete	16 wks	Mon 1/11/16	Fri 4/29/16	254FS-2 wks																		
256		Set Precast	20 wks	Mon 2/8/16	Fri 6/24/16	255SS+4 wks																		
257		Install Elevator Bank A	12 wks	Mon 6/27/16	Fri 9/16/16	256																		
258		Install Elevator Bank B	12 wks	Mon 6/27/16	Fri 9/16/16	256																		
259		Set Loading Dock Equipment	4 wks	Mon 6/27/16	Fri 7/22/16	256																		

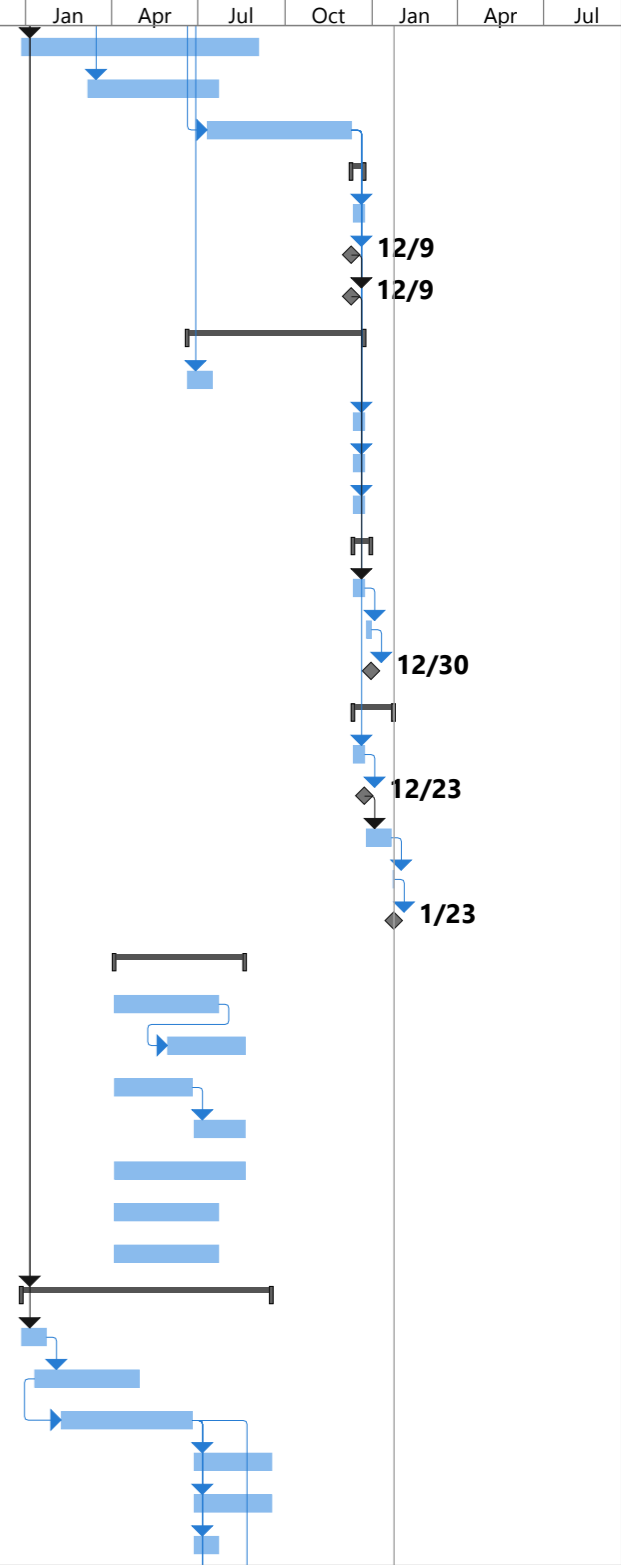

	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

