


Act ID	Description	Duration	Start	2014												2015												2016	
				J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F						
100	Phase 1	1d	18JUN14	Phase 1																									
105	Pre-Construction	36d	18JUN14 *	Pre-Construction																									
110	Bid Solicitation	10d	07AUG14 *	Bid Solicitation																									
115	Award Early Bid Packages	0	22AUG14 *	Award Early Bid Packages																									
120	Construction Coordination & Traditions Awarded Gaming	30d	25AUG14 *	Construction Coordination & Design Review																									
125	Traditions Awarded Gaming	1d	06OCT14 *	Traditions Awarded Gaming License																									
130	Construction Financing Received	1d	06OCT14 *	Construction Financing Received																									
135	Mobilization	5d	07OCT14 *	Mobilization																									
140	Steel Design & Loading	21d	06OCT14 *	Steel Design & Loading																									
145	Site Work Approval/Permit	1d	13OCT14 *	Site Work Approval/Permit																									
150	Foundation Design	30d	13OCT14 *	Foundation Design																									
155	Erosion Control Measures & Access Road	10d	14OCT14 *	Erosion Control Measures & Access Road																									
160	Clear & Grub	10d	28OCT14 *	Clear & Grub																									
161	Steel Permit	1d	04NOV14 *	Steel Permit																									
165	Site Development	210d	11NOV14 *	Site Development																									
166	Foundation Permit	1d	24NOV14 *	Foundation Permit																									
167	MEP Design	30d	24NOV14 *	MEP Design																									
170	Concrete Foundations	45d	02DEC14 *	Concrete Foundations																									
171	MEP Permit	1d	06JAN15 *	MEP Permit																									
175	Structural Steel & Slabs	90d	03FEB15 *	Structural Steel & Slabs																									
176	Offsite Improvements	21d	04MAY15 *	Offsite Improvements																									
180	Roofing	30d	12MAY15 *	Roofing																									
181	Parking Garage Build Out	90d	12MAY15 *	Parking Garage Build Out																									
185	Interior Framing & Rough In's	30d	09JUN15 *	Interior Framing & Rough In's																									
190	Exterior Skin	60d	16JUN15 *	Exterior Skin																									
195	Finishes	60d	23JUN15 *	Finishes																									
196	IT and Security	60d	29JUN15 *	IT and Security																									
200	Restaurant Services	45d	04AUG15 *	Restaurant Services																									
210	FF&E and Gaming Equipment	30d	18AUG15 *	FF&E and Gaming Equipment																									
215	Commissioning	15d	15SEP15 *	Commissioning																									
220	Training	15d	15SEP15 *	Training																									
225	System Testing	3d	28SEP15 *	System Testing																									
230	Substantial Completion	1d	30SEP15 *	Substantial Completion																									
235	Dry Run	3d	05OCT15 *	Dry Run																									
240	Certificate of Occupancy	1d	06OCT15 *	Certificate of Occupancy																									
245	Permanent Financing	1d	07OCT15 *	Permanent Financing																									

Start date	18JUN14
Finish date	08OCT15
Data date	18JUN14
Run date	20JUN14
Page number	1A
© Primavera Systems, Inc.	

**Exhibit VIII.C.20.a
Timeline for Construction
PHASE I**

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point

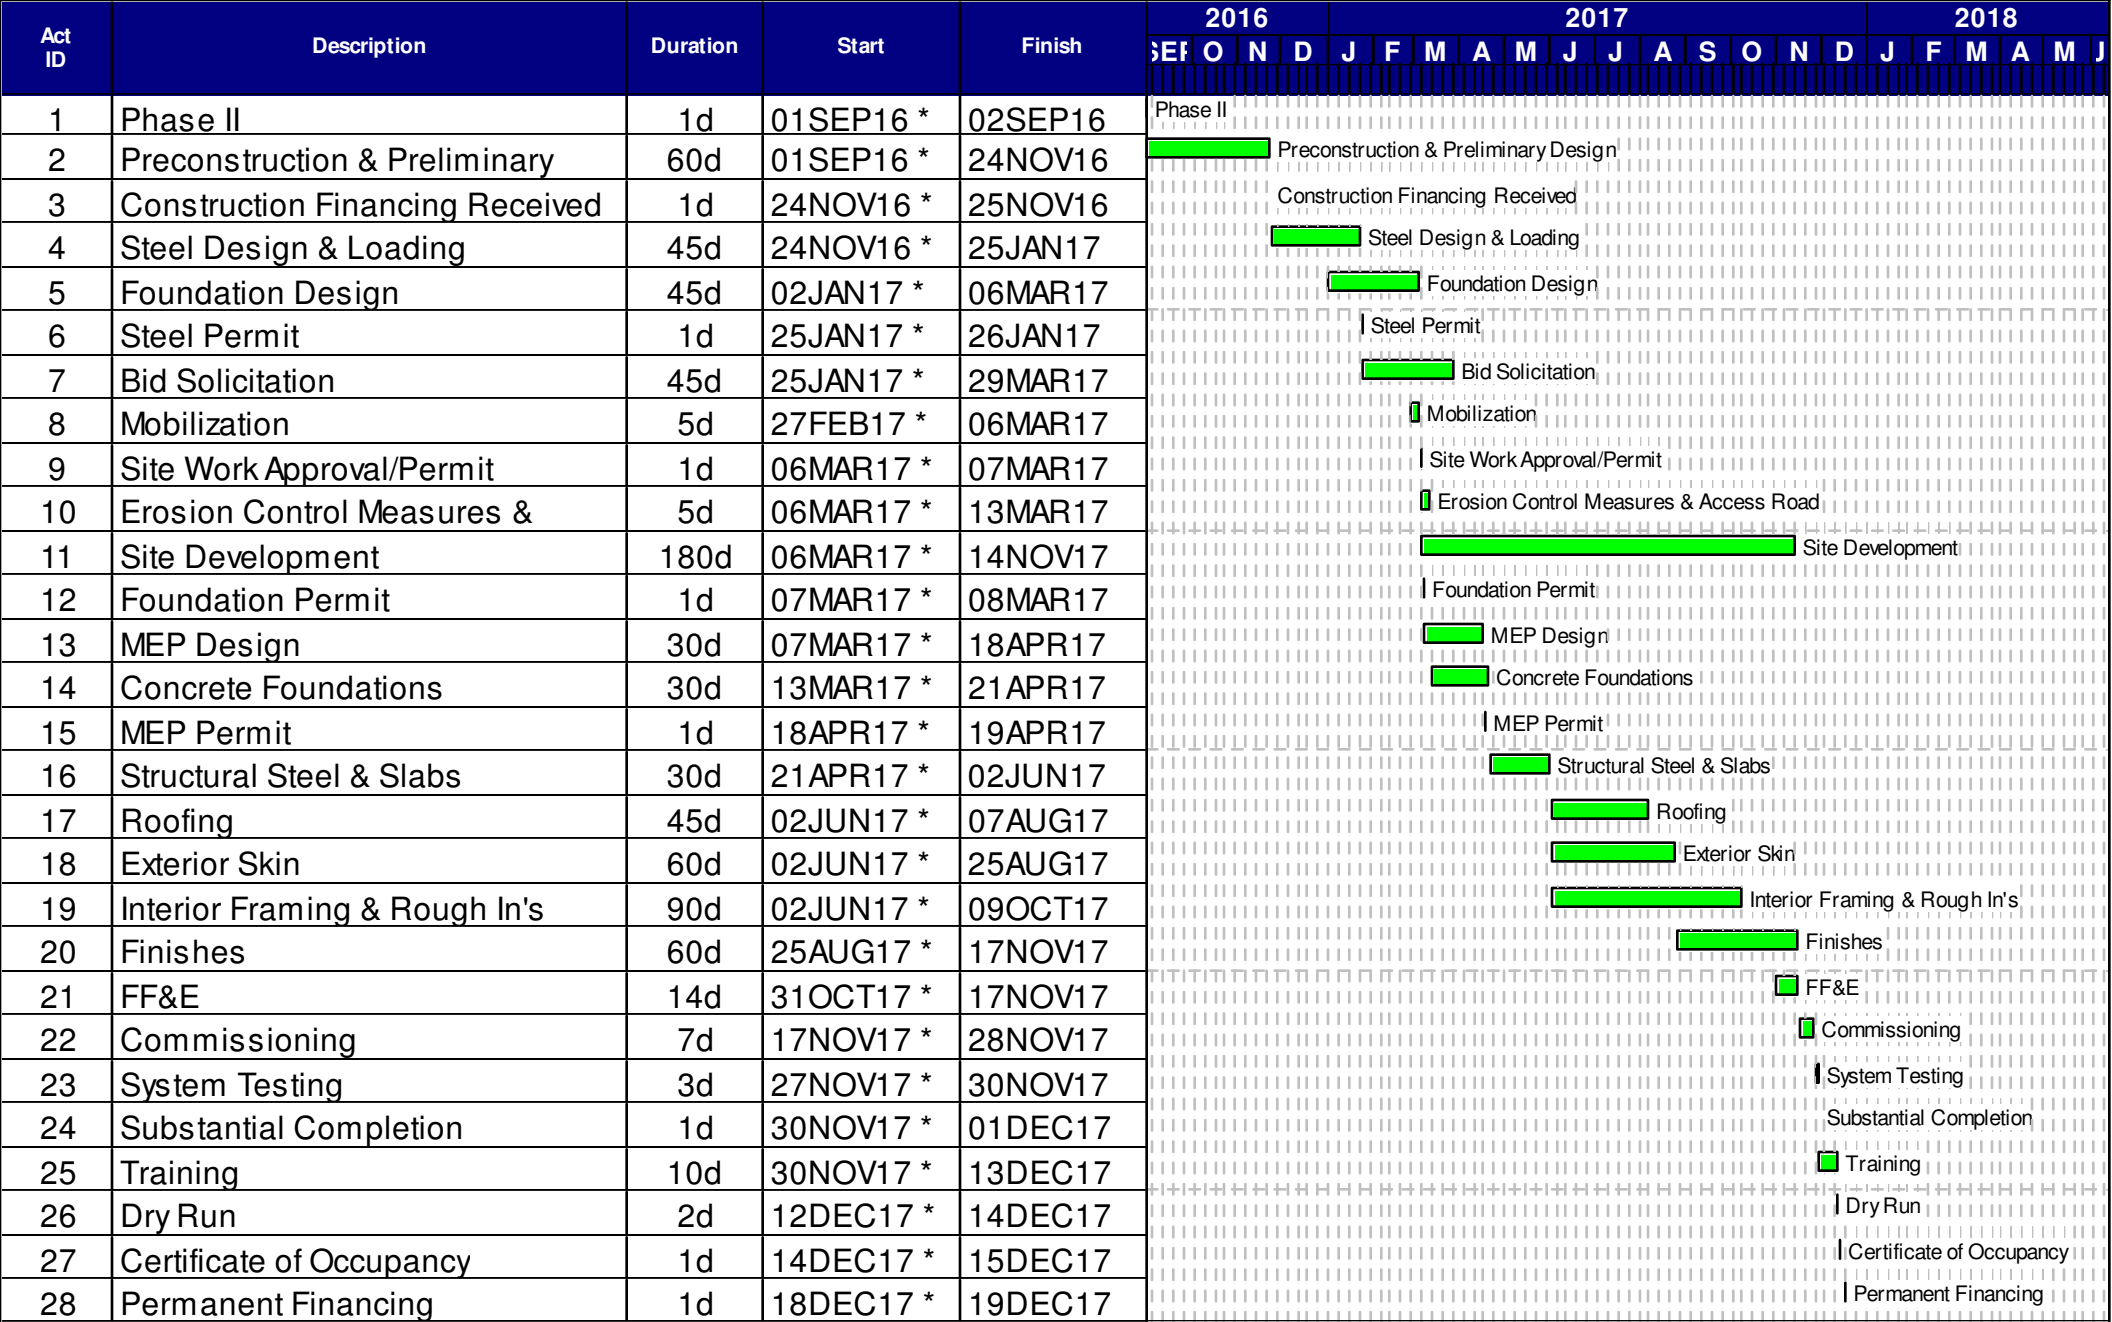

Start date 01SEP16
 Finish date 19DEC17
 Data date 01SEP16
 Run date 22JUN14
 Page number 1A
 © Primavera Systems, Inc.

**Exhibit VIII.C.20.a
 Timeline for Construction
 PHASE II**

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point
